

McCownGordon Construction

PROJECT UPDATE


City Hall | Independence, KS


March 3, 2023

SUMMARY

This week was much of the same on site with a lot of trades working in the same areas as last week.

- Gold Plumbing continued working on in wall rough-in in the basement.
- Kelley Electric continued work on in wall and soffit rough-in on the 1st floor. They also started in wall rough-in in the basement
- Myers continued working on the fire sprinkler system in the basement.
- Danny Satterfield Drywall continued hanging drywall on the 1st and 2nd floors, framed soffits on 1st floor, walls in the basement and continued mudding and taping the 2nd floor drywall.
- RetroChem continued work on repairing the historic plaster walls throughout the 1st and 2nd floors.
- McCownGordon continued working on in wall blocking on 1st floor.
- Midwest masonry set cast stone and started on brick on the storm shelter.
- Joplin Roofing started roofing the East half of the 1st floor roof.

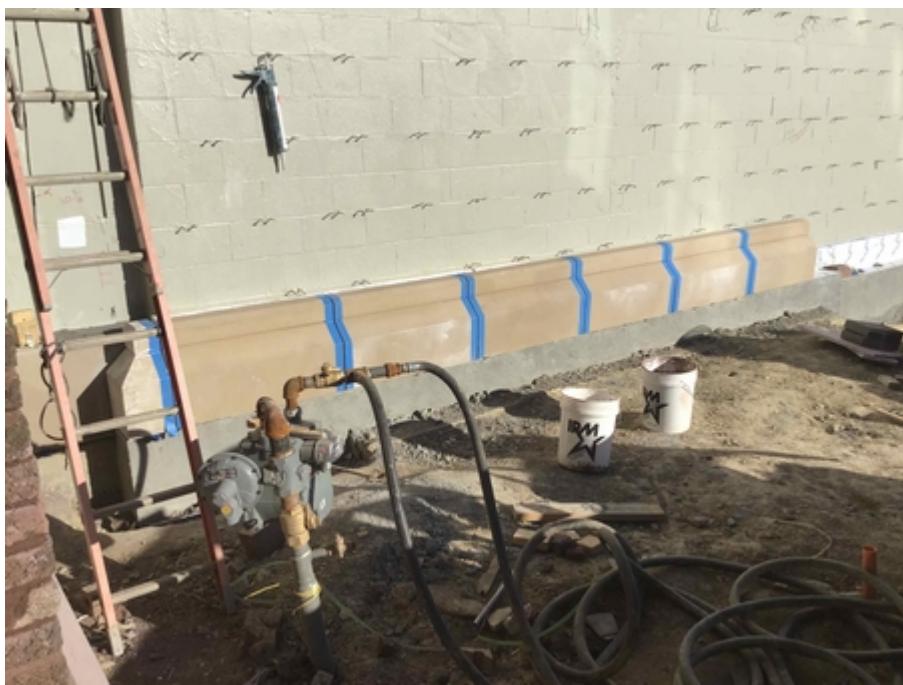

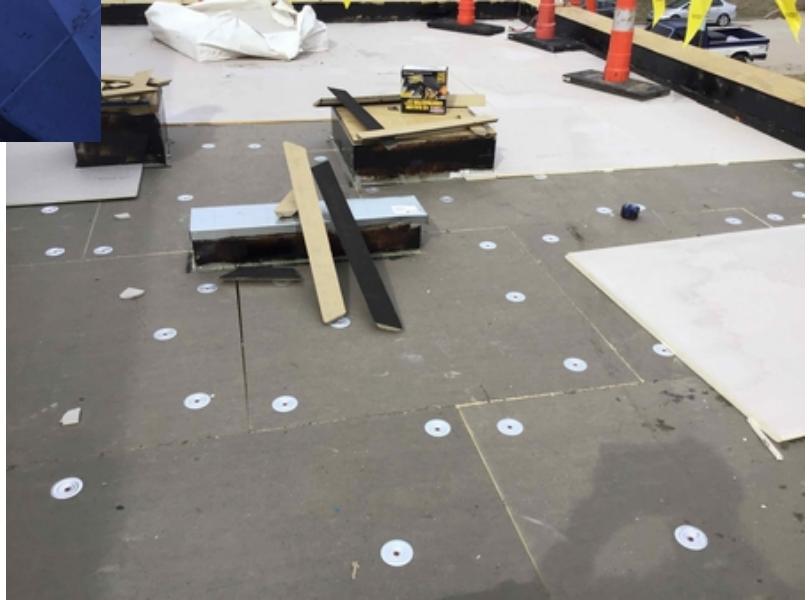

-The McCownGordon Team
