

# McCownGordon Construction

## PROJECT UPDATE


*City Hall | Independence, KS*



*February 3, 2023*

### SUMMARY

Even with the cold weather we are still moving right along and hit a couple of big milestones this past week.

- Gold Plumbing finished in wall rough in on the 2<sup>nd</sup> floor and received their inspections.
- Kelley Electric worked on in-wall and overhead rough-in on 1<sup>st</sup> and 2<sup>nd</sup> floors.
- Myers continued installing the fire sprinkler system on the 1<sup>st</sup> floor.
- Danny Satterfield Drywall started hanging drywall on the 2<sup>nd</sup> floor.
- RetroChem started work on repairing the historic plaster walls throughout the 2<sup>nd</sup> floor.
- McCownGordon finished in wall blocking on 2<sup>nd</sup> floor and started on the 1<sup>st</sup> floor.
- Gateway started installing the low voltage wiring on 2<sup>nd</sup> floor.

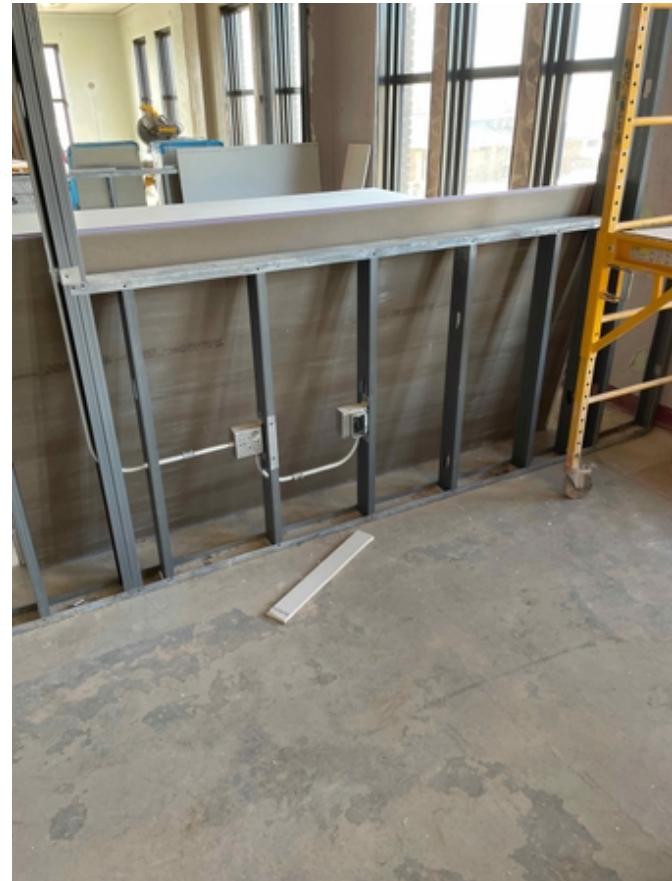

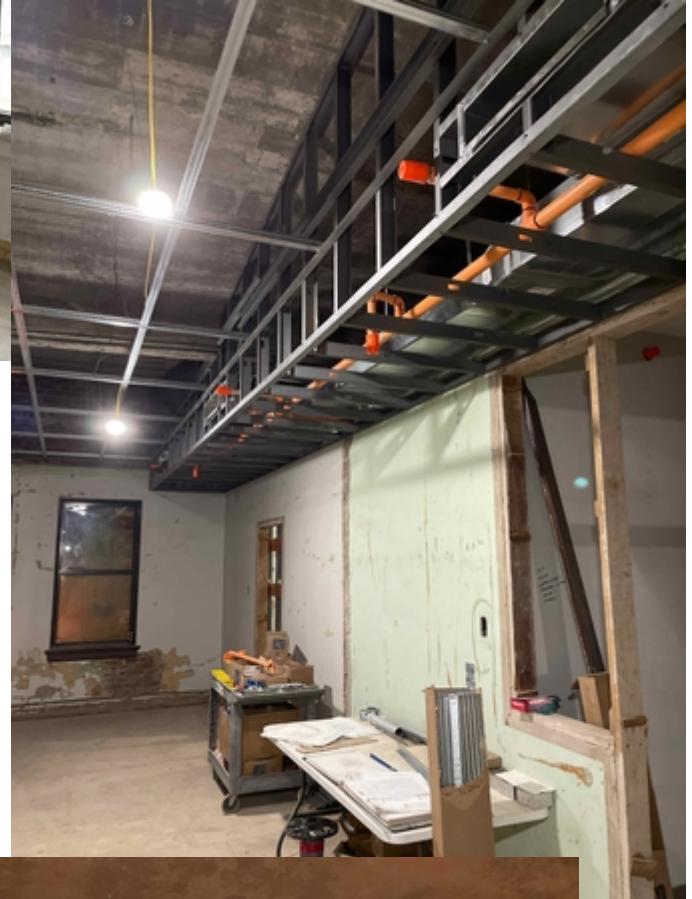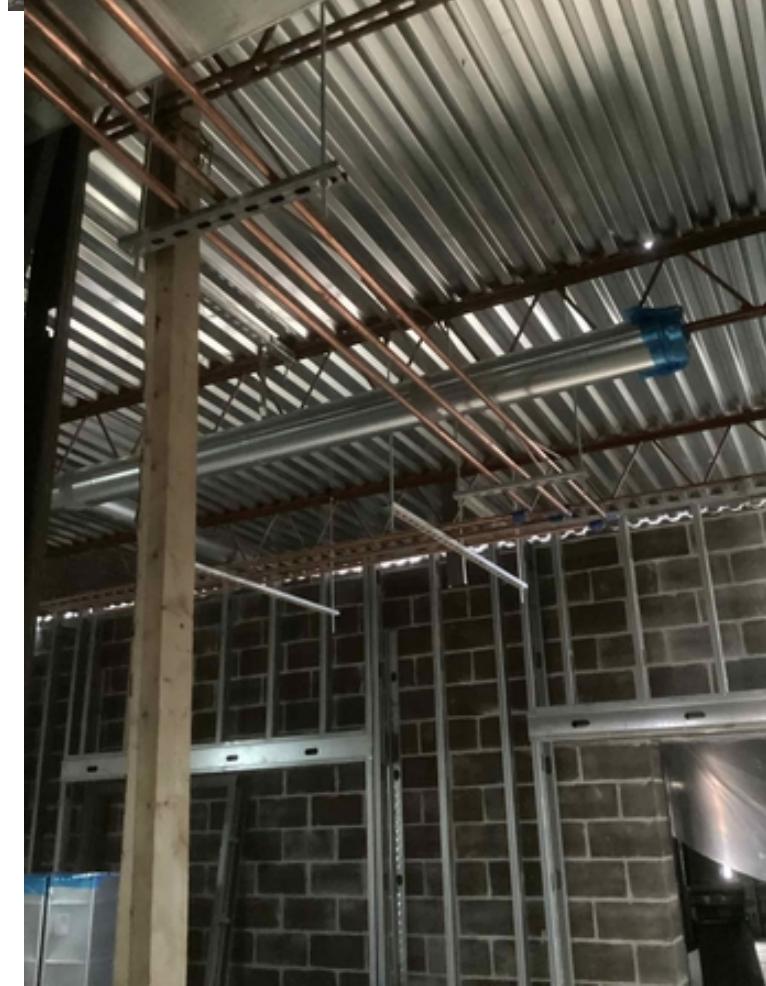

-The McCownGordon Team
