

McCownGordon Construction

PROJECT UPDATE

City Hall | Independence, KS


February 17, 2023

SUMMARY

We had another very productive week this week.

- Gold Plumbing finished in wall rough in on 1st floor and received their inspections. They started working on in wall rough in in the basement.
- Kelley Electric continued work on in wall rough in on 1st floor and lighting rough-in on 2nd floor.
- Myers continued installing the fire sprinkler system on the 1st floor.
- Danny Satterfield Drywall continued hanging drywall on the 2nd floor, framed soffits on the 1st floor and walls in the basement.
- RetroChem continued work on repairing the historic plaster walls throughout the building.
- McCownGordon worked on installed blocking for trim on 1st and 2nd floors.
- Nowak worked on site utilities and tied in the fire and water lines to the building.
- Koehn poured the patch back in Myrtle Street and the stem wall around the storm shelter.



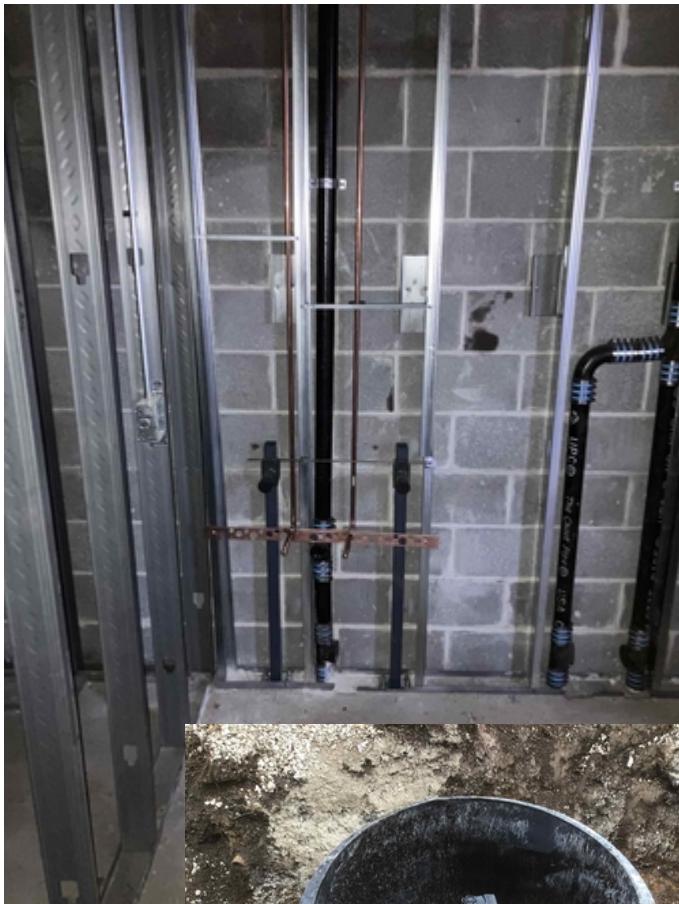

-The McCownGordon Team
